



Project Plan — TASCO Growth Platform (TASCO Insurance × VETC)

TASCO Insurance × VETC Growth Platform — Delivery & Change

iorta TechNXT

Version 1.0 · 07 October 2026

Contents

1. Objectives and success measures
2. Phases
3. Milestones
4. Gantt chart
5. Workstreams
6. Dependencies
7. Resource plan
8. Governance and reporting (summary)
9. Assumptions and constraints

Item	Value
Programme	Motor insurance growth platform: new business + renewals through the VETC ecosystem
Client	TASCO Insurance (subsidiary of Tasco JSC) with VETC as ecosystem/channel partner
Delivery partner	iorta TechNXT
Codebase	tasco-growth-platform v1.0.0 (Node.js ≥ 22.12, PostgreSQL or in-memory store)
Document owner	iorta TechNXT Delivery Lead
Status	Baseline v1.0, for Steering Committee approval

All dates are **indicative** and assume kick-off on **Monday 19 October 2026**. They are re-baselined at the end of Discovery (Gate G1). The plan explicitly protects the **Tết Nguyên Đán 2027 period (≈ 5–14 February 2027)** with a change freeze: no go-live, no pilot start and no major release in that window.

1. Objectives and success measures

The business problem the platform addresses:

Problem today	Platform response	Where in the code
Near-zero renewals through TASCO's own channels	Renewal and conquest journeys, one-tap renewal in the VETC app / Zalo	config/rules/journeys.json , src/application/journeyService.js , /api/customer/*
Weak data — roughly 1 in 10 records carries a valid policy stamp	Data enrichment and master data management (MDM) with survivorship, expiry inference, confidence and lineage; customers and the voice bot confirm expiry	config/rules/enrichment.json , src/application/ingestionService.js , POST /api/customer/expiry
Low trust in sales calls	Voice bot discloses it is automated, verifies the plate first , never asks for OTP or payment, then hands off to telesales with a summary	config/rules/content.voicebot.json , src/domain/voicebot.js
Discounts are illegal for price-regulated TNDs	Value beyond discount (roadside, e-certificate, auto-renew, inspection, claims fast-lane, add-on covers); copy guard blocks discount wording	config/rules/benefits.json , config/rules/copy_guard.json
Partners close most deals	Partner API with transparent, capped commission	/api/partner/v1/* , config/rules/commission.json
Changing business rules needs code changes	Rules studio with versioning, simulation and maker-checker approval	src/application/rulesService.js , /api/rules/*

Programme success measures. All targets are **proposed** and are confirmed at G1:

KPI	Baseline	Pilot target (proposed)	Scale target (proposed)
Renewal rate of TASCO-insured vehicles in the pilot cohort through own/VETC channels	≈ 0 %	≥ 15 %	≥ 35 %
Share of pilot renewals completed in-app (VETC app / Zalo)	n/a	≥ 50 %	≥ 65 %

KPI	Baseline	Pilot target (proposed)	Scale target (proposed)
Profiles with usable expiry (confidence ≥ 0.5)	$\approx 10\%$	$\geq 30\%$ in pilot cohort	$\geq 50\%$ of base
Taps from renewal link to e-certificate	n/a	≤ 3	≤ 3
Handoff first-contact time (voice bot → telesales)	n/a	≤ 2 business hours	≤ 1 business hour
Rule change lead time (draft → active)	weeks (code release)	≤ 1 business day	≤ 1 business day
Blocked messages caused by copy-guard violations reaching customers	n/a	0	0

2. Phases



Phase 0 — Mobilise (1 week, overlaps Discovery)

- Contract, statement of work, team onboarding, access to TASCO and VETC sandboxes.
- Repository, CI pipeline (`npm run lint`, `npm test`, `npm run test:coverage`, `npm run audit`) and environments DEV and SANDBOX (demo mode) are stood up.
- Kick-off with the Steering Committee and the RACI agreed (see [raci.md](#)).

Phase 1 — Discovery and design (2 weeks)

Week	Activities	Outputs
D1	Stakeholder interviews (TASCO business, compliance, IT; VETC product, data, call centre); review of current renewal funnel; data-sample profiling of VETC accounts and TASCO core extracts; partner landscape	As-is journey maps, data-quality baseline, regulatory constraints log
D2	To-be journeys; UX prototypes of the staff console and customer app (see <code>docs/ux/</code>); integration contracts for the VETC wallet, VETC SSO, TASCO core policy admin, Zalo ZNS, SMS brandname and the voice-AI vendor; rules inventory (all 20 rule kinds in <code>config/rules/</code>); NFRs; security threat model	Signed-off designs, integration interface agreements (IIAs), backlog with MVP scope, refined plan

Gate G1 — Design sign-off: UX prototypes accepted, IIAs signed by VETC and TASCO IT, legal positions recorded on (a) benefits wording, (b) contact policy / anti-spam, (c) PDP consent wording, (d) loyalty points and referral (currently `pending_legal_review` in `benefits.json` and `referral.json`).

Phase 2 — MVP build (8 weeks, 4 two-week sprints; can compress to 6 weeks if VETC APIs are ready at G1)

Sprint	Goal	Key backlog items
S1	Data foundation and identity	Postgres store and migrations (<code>db/migrations/001_init.sql</code>), ingestion of VETC/TASCO extracts (<code>POST /api/data/ingest</code>), golden record and DQ issues, staff sign-in with MFA, RBAC/ABAC, audit chain, staff console shell (navigation, i18n, themes, help drawer)

Sprint	Goal	Key backlog items
S2	Scoring, journeys and messaging	Explainable lead scoring and NBA, Leads and Customer 360 pages, journey engine with contact policy and copy guard, Zalo ZNS / SMS / push adapters (sandbox → real), Journeys page
S3	Purchase and voice	Quote → pay (VETC wallet) → issue (TASCO core) → e-certificate with QR, customer app (/app/), public verification (/verify/<certNo>), voice bot console and campaign, telesales inbox with handoffs
S4	Governance, partners, claims, operations	Rules studio (maker-checker, simulate), partner onboarding and API keys, partner API, commission statements, claims FNOL queue, DSAR, governance and adoption dashboards, Operations page (jobs, integrations status), hardening, performance tests (npm run test:perf)

Gate G2 — Build complete: all MVP stories meet the Definition of Done (see [delivery-methodology.md](#)); coverage $\geq 80\%$ lines and functions and $\geq 70\%$ branches (enforced by `npm run test:coverage`); no open critical or high findings from SAST/DAST or `npm audit`; WCAG 2.2 AA checks passed on the core flows.

Phase 3 — SIT and UAT (3 weeks)

Week	Focus
T1	System integration testing against VETC and TASCO UAT endpoints: wallet debit/refund idempotency, policy issuance and compensation, SSO token exchange, ZNS template delivery, telephony. Reconciliation job (<code>POST /api/ops/jobs/reconciliation</code>) proven.
T2	User acceptance testing by role, using the persona manuals in <code>docs/manuals/</code> as test scripts; usability tests with telesales agents and customers (see <code>docs/ux/usability-testing-plan.pdf</code>); penetration test by an independent party
T3	Defect fixing, regression, operational readiness review (runbooks, on-call, DR test), training of pilot users, data load of the pilot cohort

Gate G3 — Go / No-go for pilot: UAT sign-off by the TASCO business owner; compliance sign-off of scripts, templates and benefits; security sign-off; operational acceptance by the support team; Zalo ZNS templates approved by Zalo.

Phase 4 — Pilot (4 weeks, Hà Nội + TP. Hồ Chí Minh)

- Proposed cohort: TASCO-insured and conquest vehicles registered in Hà Nội and TP.HCM with expiry in the next 15–60 days, plus lapsed vehicles (≤ 60 days), capped at an agreed volume of **50k–100k vehicles** (consistent with `docs/business/07-commercials-and-engagement-model.pdf`).
- Two telesales squads (one per city) using the telesales inbox, plus a supervisor per squad. Agents `agent.hn` and `agent.hcm` in the demo data mirror this setup.
- Weekly pilot review covering funnel, contact-policy blocks, voice bot outcomes, plate-verification failure rate, opt-out rate, CSAT and defects.
- A/B design: control group with business-as-usual reminders, test group with full journeys.

Gate G4 — Scale decision: pilot KPIs against targets, no unresolved regulatory issue, unit economics from `/api/dashboard/overview` (`economics` block) validated with contracted rates in `config/rules/costs.json`.

Phase 5 — Scale-out (waves)

Wave	Scope	Indicative timing
W1	All provinces, car TNDs renewal + conquest + lapsed recovery	Pilot end + 2 weeks
W2	Partner API live with the first partners (bank, showroom, inspection centre); new-vehicle journey from <code>vetc.tag_activated</code> events	W1 + 4 weeks
W3	Add-on covers at scale (PA per seat, physical damage with inspection flow), motorbike TNDs in the app, loyalty points and referral only if legally approved	W2 + 6 weeks
W4	Advanced analytics (ML model behind the scoring port, with bias monitoring), LLM-assisted intent classification behind the NLU port	Roadmap


Hypercare runs for **4 weeks after each wave**, followed by BAU support and the knowledge transfer described in [kt-plan.md](#).

3. Milestones

ID	Milestone	Indicative date	Evidence / gate criteria	Approver
M 0	Kick-off	19 Oct 2026	Signed SoW, RACI accepted	SteerCo
M 1	Discovery complete (G1)	30 Oct 2026	Signed designs, IIAs, legal positions log	TASCO Business Owner, VETC Product Owner, Compliance
M 2	Sprint 1 demo: data and identity	13 Nov 2026	Ingestion of real sample, MFA login, audit chain verifies (<code>GET /api/audit/verify</code>)	Product Owner
M 3	Sprint 2 demo: scoring and journeys	27 Nov 2026	Explainable scores, journey dry run with contact policy	Product Owner
M 4	Sprint 3 demo: one-tap purchase and voice	11 Dec 2026	End-to-end renewal in ≤ 3 taps, e-certificate QR verifies	Product Owner, VETC App Lead
M 5	Build complete (G2)	25 Dec 2026	DoD met, quality gates green	Delivery Lead, TASCO IT
M 6	SIT complete	8 Jan 2027	All integration test cases passed	TASCO IT, VETC IT
M 7	UAT sign-off, Go/No-go (G3)	22 Jan 2027	UAT, security and compliance sign-offs	SteerCo
—	T&T change freeze	1 – 14 Feb 2027	No production change except emergency fixes	CAB
M 8	Pilot start	25 Jan 2027 (soft launch, low volume) / full volume 15 Feb 2027	Pilot cohort loaded, squads trained	SteerCo
M 9	Pilot review (G4)	12 Mar 2027	Pilot report, scale decision	SteerCo

ID	Milestone	Indicative date	Evidence / gate criteria	Approver
M 10	Scale-out W1 live	29 Mar 2027	Nationwide car TNDs	SteerCo
M 11	Partner API live (W2)	26 Apr 2027	First 3 partners transacting	Partner Manager, Compliance
M 12	KT complete, BAU handover	W2 + 8 weeks	KT sign-off criteria met	TASCO IT Head

4. Gantt chart

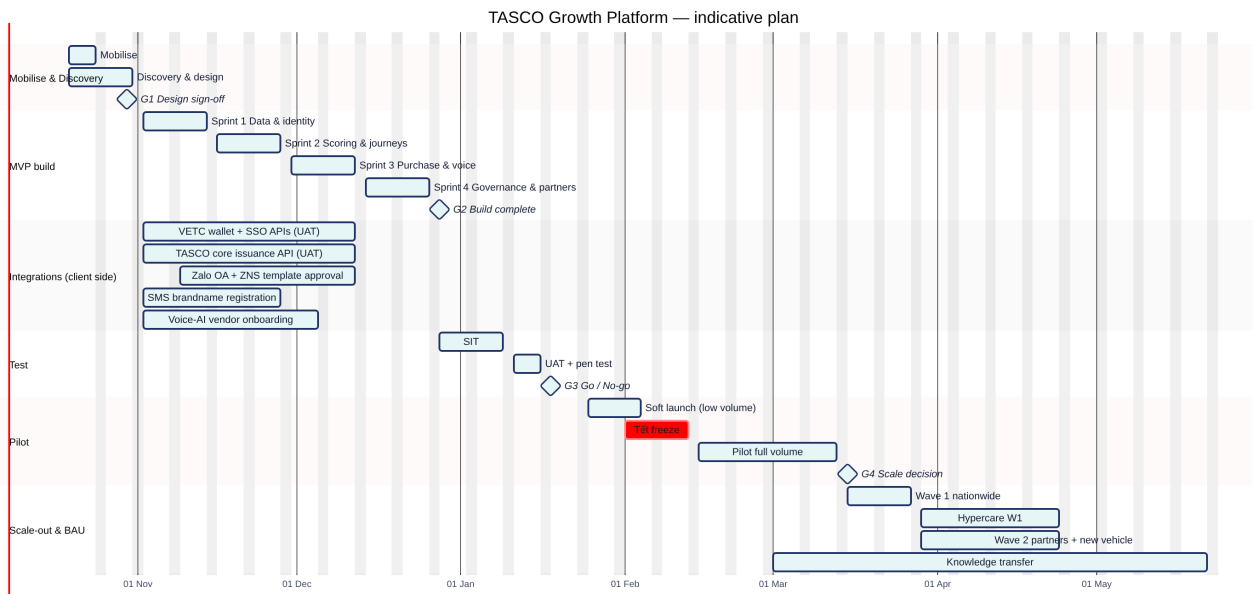

5. Workstreams

#	Workstream	Lead (accountable)	Scope
WS 1	Product and business change	TASCO Product Owner	Backlog, priorities, business rules content, pilot design, KPIs
WS 2	Data and MDM	iorta Data Engineer + VETC Data Lead	Extracts, ingestion, enrichment rules, DQ triage, lineage, data steward process
WS 3	Platform engineering	iorta Solution Architect	Backend services, rules engine, journeys, voice bot, purchase flow, partner API
WS 4	Experience (UX/UI)	iorta UX Lead	Staff console, customer app, verification page, design system, accessibility
WS 5	Integrations	iorta Integration Engineer + TASCO IT + VETC App Lead	VETC wallet, SSO and events; TASCO core; Zalo OA/ZNS; SMS; telephony/voice AI
WS 6	Security, privacy and compliance	TASCO CISO + Compliance	Threat model, pen test, PDP (Decree 13/2023/ND-CP), anti-spam (Decree 91/2020/ND-CP), Law on Insurance Business 08/2022/QH15, DPIA

#	Workstream	Lead (accountable)	Scope
WS 7	Quality engineering	iorta QA Lead	Test strategy, automation, performance, accessibility, UAT coordination
WS 8	DevSecOps and operations	iorta DevSecOps	CI/CD, environments, observability (/metrics , /health/*), backups, DR, runbooks
WS 9	Change, training and adoption	TASCO Change Lead + iorta BA	Change impact, communications, training, champions (see change-management-and-training.md)
WS 10	Partner channel	TASCO Partner Manager	Partner selection, commercial terms, onboarding and API certification

6. Dependencies

ID	Dependency	Provider	Needed by	Impact if late	Mitigation
D-01	VETC data extract (accounts, vehicles, tags, toll class, app activity) with a legal basis for processing	VETC Data + Legal	S1 start	No real data for scoring; pilot cohort cannot be selected	Synthetic generator (<code>src/adapters/integrations/syntheticVetcSource.js</code>) keeps build moving; data-sharing agreement drafted in Discovery
D-02	VETC wallet debit/refund API with idempotency	VETC IT	S3	No one-tap payment	Sandbox gateway (<code>mockGateways.js</code>) with the same port contract; contract tests
D-03	VETC SSO token exchange for the in-app webview	VETC App	S3	Customer app limited to signed renewal links	Signed links (<code>/app/?r=...</code>) already work independently of SSO
D-04	VETC app release slot (entry point, deep link, push)	VETC App	Pilot	Customers cannot reach the app journey	Zalo OA mini app and SMS links as fallback channels
D-05	VETC ecosystem events (<code>vetc.tag_activated</code> , <code>vetc.inspection_booked</code> , <code>vetc.wallet_topped_up</code> , <code>vetc.long_trip_started</code>)	VETC IT	W2	No moment-of-truth triggers	Batch replay through <code>POST /api/ecosystem/events</code>
D-06	TASCO core policy admin issuance API and certificate numbering	TASCO IT	S3	No issuance	Sandbox issuance; reconciliation job finds mismatches
D-07	Zalo OA verification and ZNS template approval (each template in <code>content.messages.json</code>)	Zalo / VNG, VETC Marketing	Pilot –2 weeks	No Zalo channel	Submit templates in S2; push and SMS fall back automatically through journey channel order
D-08	SMS brandname registration (VETC / TASCO) with the carriers	SMS vendor, VETC	Pilot –2 weeks	No SMS channel	Use an existing VETC brandname
D-09	Voice-AI vendor (ASR/TTS for Vietnamese northern, central and southern accents), SIP trunk, call recording	Vendor	S3	Voice bot only in console mode	Console mode (<code>/api/voice/sessions</code>) for testing; telesales-only fallback

ID	Dependency	Provider	Needed by	Impact if late	Mitigation
D-10	Legal opinions: benefits wording, loyalty points, referral, contact frequency, consent text	TASCO Legal / Compliance	G1 (initial), G3 (final)	Features held back	Feature flags via <code>legalStatus</code> and <code>enabled</code> fields in rules; only approved benefits reach customers
D-11	TASCO IdP (Azure AD / Keycloak via OIDC) for staff SSO	TASCO IT	Scale-out	Local accounts with TOTP remain	Token contract unchanged (identity service comment, ADR-007)
D-12	Production hosting, PostgreSQL, secrets (<code>JWT_SECRET</code> , <code>DATA_KEYS</code> , <code>BLIND_INDEX_KEY</code>)	TASCO IT / cloud provider	SIT	No production-like test	Production config refuses to boot without secrets — tested in SIT
D-13	Partner commercial agreements and Ministry of Finance commission caps confirmed	TASCO Finance / Legal	W2	Partner API cannot go live	Caps enforced in <code>commission.json</code> (<code>statutoryCaps</code>) and by validators

7. Resource plan

7.1 iorta TechNXT team (FTE by phase)

Role	Discovery	Build	SIT/UAT	Pilot	Scale-out / Hypercare
Delivery Lead	1	1	1	1	0.5
Solution Architect	1	1	0.5	0.5	0.25
Business Analyst	1.5	1	1	0.5	0.5
UX/UI Designer	1	1	0.5	0.5	0.25
Backend Engineers (Node.js)	1	3	2	1.5	1
Frontend Engineers	0.5	2	1.5	1	0.5
Data Engineer	1	1	0.5	0.5	0.5
Integration Engineer	0.5	1	1	0.5	0.25
QA Engineers (manual + automation)	0.5	2	2	1	0.5
DevSecOps Engineer	0.5	1	1	1	0.5
Data Scientist (scoring, bias monitoring)	0.25	0.5	0.25	0.5	0.5
Total	8.75	14.5	11.25	8.5	5.25

7.2 Client-side commitments (minimum)

Organisation	Role	Commitment
TASCO	Business Owner (sponsor)	SteerCo, gates
TASCO	Product Owner	100 % during Build to Pilot

Organisation	Role	Commitment
TASCO	Compliance / Legal	2 days per week; rule approver role (<code>rule_approver</code> , <code>compliance_officer</code>)
TASCO	IT integration lead and core-system engineer	50 % during Build and SIT
TASCO	CISO / security analyst	Threat model, pen-test scoping, sign-off
TASCO	Underwriting / actuarial	Confirms tariffs (<code>tariff.*</code>) and illustrative rates (<code>rating.motor_pd</code> , <code>rating.pa_seat</code>) before go-live
TASCO	Claims lead	FNOL process, claims handler role
VETC	Product Owner	50 %
VETC	App lead + 2 mobile engineers	Entry point, deep links, SSO, wallet confirmation UX
VETC	Data engineer	Extracts, events
VETC	Call-centre / telesales manager + 2 supervisors + pilot agents	Training, pilot operations

7.3 Environments

Env	Purpose	Data	Demo mode
DEV	Developer integration	Synthetic (<code>SEED_RECORDS</code>)	On
SANDBOX / TRAINING	Demos, training, usability tests	Synthetic, reset nightly with <code>npm run seed</code>	On (<code>/api/demo/totp:username</code> available)
SIT	Integration with VETC/TASCO UAT	Masked production-like	Off
UAT	Business acceptance	Masked production-like	Off
PROD	Live	Real	Off — the server refuses to start with <code>DEMO_MODE</code> in production unless explicitly overridden

8. Governance and reporting (summary)

- **Steering Committee** every 2 weeks during Build to Pilot, then monthly. It is chaired by the TASCO Business Owner, with the VETC Product Director, the TASCO CIO and Compliance Head, and the iorta TechNXT Engagement Director.
- **Design Authority** meets weekly and owns architecture decisions, integration contracts and security exceptions.
- **Change Advisory Board (CAB)** owns production changes and RBAC changes (`config/security/rbac.json` is changed only through code review plus CAB). Business rules do **not** go through CAB, because they follow maker-checker in the Rules studio.
- Weekly status report: RAG, burn-up, milestone forecast, top risks from [risk-register.md](#), decisions needed.

The full governance model is in [delivery-methodology.md](#).

9. Assumptions and constraints

1. The MVP scope is the capability already present in the v1 codebase. Build effort focuses on productionising: real adapters, UI, hardening, data migration and test automation.
2. TNDs premiums follow Decree 67/2023/ND-CP (`tariff.tnds_car.json` , `tariff.tnds_motorbike.json`). TASCO underwriting confirms the tariffs before go-live.
3. Rates for physical damage and personal accident in the repository are **illustrative** and must be replaced through the Rules studio before sale.
4. No discount, rebate or cashback is offered on price-regulated products. Value comes from services.
5. Loyalty points and referral stay disabled until legal approval.
6. Hosting is in Vietnam or an approved region, in line with data localisation requirements under the PDP decree and the Cybersecurity Law. This is to be confirmed by TASCO Legal.
