



Delivery Methodology

TASCO Insurance × VETC Growth Platform — Delivery & Change

iorta TechNXT

Version 1.0 · 07 October 2026

Contents

1. Why hybrid
2. Lifecycle overview
3. Scrum framework
4. Definition of Ready (DoR)
5. Definition of Done (DoD)
6. Quality gates
7. Environments and promotion
8. Governance cadence
9. Reporting
10. Tooling

Document	Version	Date	Owner	Status
Delivery Methodology	1.0	07 October 2026	iorta TechNXT — Delivery Lead	Issued for submission


Approach: hybrid agile. We run Scrum for product increments and add **stage gates** for the regulated items that cannot simply be "iterated into production" in an insurance business: tariffs, customer-facing wording, consent, contact policy, partner commission, security and privacy.

The aim is fast, visible progress every two weeks, while every change that affects customers, money or personal data is approved by the right person before it reaches production, with evidence kept in the audit trail.

1. Why hybrid

Concern	Pure agile risk	Hybrid answer
Regulated premiums (TNDS, Decree 67/2023)	Rates changed by a developer in a sprint	Tariffs are rule sets with maker-checker approval (<code>rulesService.approve</code> refuses self-approval). Underwriting is the checker.
Discount prohibition (Law 08/2022/QH15)	Marketing copy shipped without review	Copy guard (<code>copy_guard.json</code>) blocks banned phrases at validation and at send time. Content changes need a Compliance approver.
Anti-spam (Decree 91/2020) and PDP (Decree 13/2023)	Journeys contacting customers too often or without consent	<code>contact_policy</code> rule set enforced in <code>canContact()</code> . Legal approves policy values at G1 and G3.
Integration with VETC and TASCO core	Late surprises	Integration contracts frozen at G1. Sandbox adapters implement the same ports, and contract tests run in CI.
Security	Findings discovered after go-live	Security gates in the DoD and at G2/G3. RBAC changes go through code review plus CAB.

2. Lifecycle overview

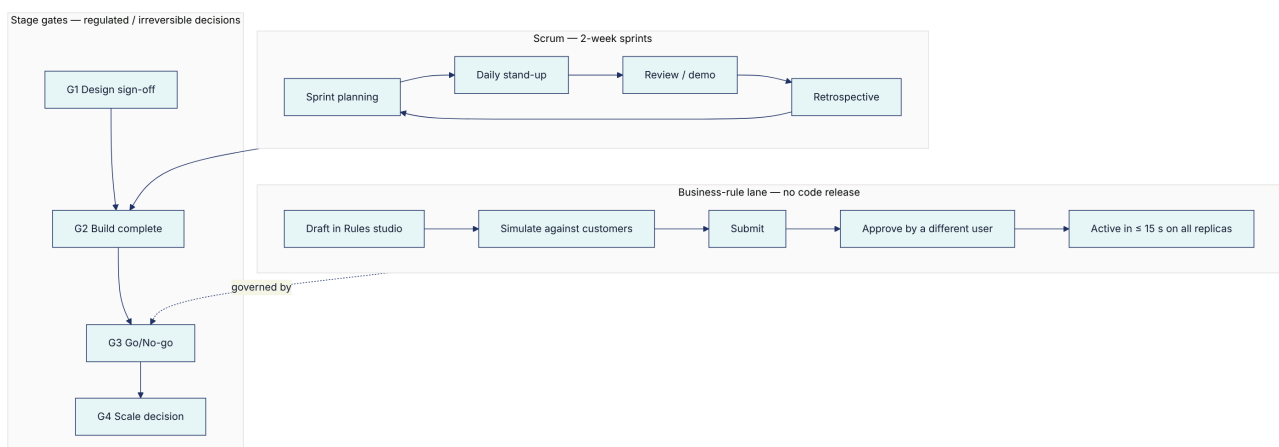

There are three lanes of change, each with its own path to production:

Lane	Examples	Path	Approver
Code	New page, new adapter, bug fix	Pull request → CI quality gates → staging → CAB (for production)	Tech lead (code review) + CAB
Security configuration	config/security/rbac.json, MFA_REQUIRED_ROLES, secrets	Pull request with Security review → CAB	CISO delegate
Business rules	Scoring weights, NBA, journeys, benefits, templates, voice script, tariffs, commission, contact policy, retention	Rules studio: draft → validate → simulate → submit → approve	Rule approver or compliance officer (four-eyes, enforced in code). Restricted kinds need a compliance officer.

3. Scrum framework

3.1 Roles

- **Product Owner (TASCO)** owns the backlog and accepts stories.
- **Scrum Master / Delivery Lead (iorta TechNXT)** owns the process, impediments and reporting.
- **Development team (cross-functional)**: backend, frontend, data, QA, DevSecOps, UX and BA.
- **Client SMEs** attend refinement and reviews: VETC product, compliance and telesales supervisors.

3.2 Ceremonies

Ceremony	When	Duration	Participants	Output
Sprint planning	Day 1 of sprint	2 h	Team, PO	Sprint goal, committed backlog
Daily stand-up	Daily 09:15 ICT	15 min	Team (PO optional)	Impediments raised
Backlog refinement	Weekly, Wed	1.5 h	PO, BA, Architect, QA, UX	Stories meeting DoR
Design review	Weekly, Thu	1 h	UX, PO, FE, Accessibility champion	Approved designs
Sprint review / demo	Last day of sprint	1.5 h	Team, PO, stakeholders (TASCO, VETC)	Accepted increment, feedback
Retrospective	Last day of sprint	1 h	Team	Two or three improvement actions
Rules clinic	Weekly, Tue	45 min	Rule authors, approvers, BA	Draft rule changes reviewed before submission
Integration sync	Twice weekly	30 min	iorta Integration, VETC IT, TASCO IT	Contract changes, environment issues
Release readiness	Before each release	45 min	DevSecOps, QA, PO, Support	Go/no-go for the release

3.3 Sprint cadence

Sprints last two weeks. A potentially shippable increment is deployed to SANDBOX at the end of each sprint for stakeholder exploration, with demo mode and synthetic data. During Pilot and Scale-out the cadence moves to **weekly releases** with feature flags.

4. Definition of Ready (DoR)

A story may enter a sprint when **all** of the following are true:

1. It is written as a user story with the persona named (for example, "As a telesales agent...") and refers to a page in the Journey Maps and Information Architecture document (docs/ux/journey-maps-and-information-architecture.pdf).
2. Acceptance criteria are written in Given/When/Then, including at least one negative case: permission denied, validation error or business-rule violation.
3. The required permission is identified (for example `handoff:work`) and mapped to roles in `config/security/rbac.json`. Any change to that file is flagged for Security review.
4. UX design is approved, or explicitly "no UI change", with Vietnamese and English copy supplied. The copy is checked against the content style guide (no discount wording).
5. Data needs are known: fields, PII classification and masking rule (`profile:read_pii`).
6. Any integration dependency has a contract in place or a sandbox adapter.
7. Any regulated element is tagged `REG` and has a named approver (Compliance, Underwriting, Legal).
8. The story is estimated and small enough for one sprint.

5. Definition of Done (DoD)

A story is done only when **all** applicable items are met:

#	Criterion	How verified
1	Code merged to main through a pull request reviewed by at least one engineer other than the author	Git host branch protection
2	Lint clean	<code>npm run lint</code> in CI
3	Unit, integration, API, security and functional tests written and passing. Each Given/When/Then acceptance scenario has a functional test in <code>test/functional</code> .	<code>npm test</code>
4	Coverage ≥ 80 % lines and functions, ≥ 70 % branches	<code>npm run test:coverage</code> (thresholds enforced by the script)
5	Security tests pass, with no new critical or high findings	<code>npm run test:security</code> , SAST, secret scan, <code>npm run audit</code> (high and above fail the build)
6	DAST baseline scan on SANDBOX for changed endpoints	ZAP baseline in pipeline
7	Authorisation tested: allowed role succeeds, other roles get 403	API tests per route
8	Accessibility checks: automated (axe) with zero serious or critical issues, keyboard-only walkthrough, screen-reader smoke test (NVDA or VoiceOver) on changed screens	QA checklist in the UX Standards and Accessibility document
9	Vietnamese and English strings present; dates dd/mm/yyyy; VND formatting	UI review
10	Performance budget respected (page and API p95, see UX standards)	<code>npm run test:perf</code> for API changes, Lighthouse for UI
11	Audit events emitted for every state change affecting customers, money, access or rules	Test asserts the audit entry
12	OpenAPI regenerated if routes changed	<code>npm run job -- openapi</code> writes <code>docs/api/openapi.json</code>

#	Criterion	How verified
13	Documentation updated: user manuals in <code>docs/manuals/</code> , contextual help text, runbooks and ADRs where relevant	PR checklist
14	Demo data / seed updated if needed (<code>src/bootstrap/seed.js</code>)	Sandbox smoke test
15	PO acceptance in the sprint review	Story status

Definition of Done for a business-rule change (Rules studio lane):


1. Payload validates (`POST /api/rules/validate` returns no errors). This includes JSON Logic and decision-table checks, commission caps and the copy guard.
2. Simulation evidence is recorded (`POST /api/rules/simulate`) on at least five representative customers for the kinds `scoring`, `nba`, `journeys` and `benefits`. The before/after outcome is attached to the change ticket.
3. A description explains the business reason and expected impact.
4. The change is submitted by its author and approved by a **different** user with `rules:approve`. Changes to `abac`, `copy_guard`, `contact_policy`, `commission` and `retention` are approved by a compliance officer (enforced in code).
5. After activation, the expected KPI movement is monitored for 7 days and a rollback plan is known. Rollback creates a new draft that also needs approval.

6. Quality gates

Gate	Where	Pass criteria	Blocking?
QG1 Commit	Pre-commit / PR	Lint, unit tests	Yes
QG2 Pull request	CI	All tests, coverage thresholds, <code>npm run audit</code> , secret scan, SAST	Yes
QG3 Integration	Nightly on SIT	Contract tests against VETC/TASCO UAT, Postgres tests (<code>npm run test:pg</code>)	Yes for release
QG4 Release candidate	Staging	Regression pack, DAST, performance (<code>npm run test:perf</code>), accessibility pack, OpenAPI diff reviewed	Yes
QG5 Production	CAB	Release notes, rollback plan, runbook updates, on-call confirmed, change window (not in Tét freeze)	Yes
QG6 Stage gate	SteerCo	Gate criteria in the project plan	Yes

Quality metrics are tracked every sprint: escaped defects, defect density, coverage trend, mean time to restore (MTTR), accessibility issues open, security findings by severity and age.

7. Environments and promotion



Environment rules:

- `DEMO_MODE` is off by default. It is **on** only in DEV, CI, SANDBOX and the hosted UAT (`NODE_ENV=uat`), never in STAGING or PRODUCTION. The demo TOTP endpoint behind **Sign in with demo code (UAT)** returns 404 when demo mode is off.
- UAT -only settings (`DEMO_PASSWORD` , `DEMO_TOTP_SEED` , `DEMO_ACCOUNT_SYNC`) are set only in the hosted UAT. The UAT password is distributed in the access workbook and is never written in documents.
- Production secrets come from the secret manager through the `<NAME>_FILE` convention (`src/shared/config.js`). Production refuses to boot without them, and without `DATABASE_URL` .
- Rule sets are promoted **through the Rules studio in each environment**, not by copying the database. Baseline rule files in `config/rules/` seed new environments only (`npm run job -- rules` loads kinds that have no version yet).
- Production data is never copied to lower environments unmasked.

8. Governance cadence

Forum	Frequency	Chair	Members	Decides
Steering Committee	Every 2 weeks (Build to Pilot), monthly after	TASCO Business Owner	VETC Product Director, TASCO CIO, TASCO Head of Compliance, iorta Engagement Director, Delivery Lead	Gates, scope, budget, top risks, escalations
Design Authority	Weekly	iorta Solution Architect	TASCO IT architect, VETC IT, Security	Architecture, integration contracts, NFRs, ADRs
Rules Governance Board	Fortnightly (and ad hoc)	TASCO Compliance	Product, Underwriting, Marketing, Data Steward	Policy-level rule changes (contact policy, benefits legal status, tariffs), review of rule change log
Change Advisory Board	Weekly + emergency	TASCO IT Service Manager	DevSecOps, Support, Security	Production releases, RBAC changes
Data Governance Forum	Monthly	TASCO Data Owner	VETC Data, Data Steward, DPO	DQ KPIs, source trust weights (<code>enrichment.json</code>), retention, DSAR metrics
Pilot war-room	Daily during pilot weeks 1–2, then twice weekly	TASCO Product Owner	Telesales supervisors, Support, iorta	Operational issues, quick fixes

Escalation path

Team → Delivery Lead / PO (within 1 day) → Design Authority or Rules Governance Board (within 3 days) → Steering Committee (next session, or ad hoc for red items).

9. Reporting

Report	Audience	Frequency	Content
Weekly status	PO, SteerCo members	Weekly (Friday)	RAG by workstream, burn-up, milestones, top 10 risks and issues, decisions needed
Sprint report	PO, team	Per sprint	Goal met?, velocity, scope change, quality metrics, demo recording
SteerCo pack	SteerCo	Per session	Gate readiness, budget, risk heat map, KPI trend (from <code>/api/dashboard/overview</code> and <code>/api/dashboard/adoption</code>)
Pilot dashboard	SteerCo, business	Live + weekly digest	Funnel by journey and channel, renewals in-app vs telesales, voice outcomes, opt-out and plate-verification failure rates, contact-policy blocks, CSAT
Governance report	Compliance, Audit	Monthly	Rule changes with maker and checker, audit-chain verification result (<code>/api/audit/verify</code>), DSAR volumes and turnaround, access reviews
Service report	TASCO IT	Monthly (BAU)	Availability, incidents, MTTR, job success (<code>/api/ops/jobs</code>), integration circuit-breaker trips

RAG definitions: **Green** means on track. **Amber** means at risk, with a recovery plan owned by the workstream. **Red** means a milestone or gate will be missed without a SteerCo decision.

10. Tooling

Purpose	Tool (proposed; adopt client standard where one exists)
Backlog and sprints	Jira (or Azure Boards)
Source and CI	Git host with branch protection, CI pipeline (<code>.github/workflows/ci.yml</code>) executing the <code>package.json</code> scripts
Documentation	<code>docs/</code> in the repository (versioned with the code), delivered as Word and PDF + Confluence for meeting notes
Design	Figma (design tokens exported to CSS variables, see the Design System, <code>docs/ux/design-system.pdf</code>)
Observability	Prometheus scraping <code>/metrics</code> , log aggregation of structured JSON logs (with <code>requestId</code>), alerting
Test management	Xray / TestRail, with UAT scripts derived from <code>docs/manuals/</code>
